Activity ID	Activity Description	Orig Dur	Resp	Early Start	Early Finish	Total Float
Milestones						
MI1000	Notice Of Award	0	MI	25SEP03		-24
MI1010	Notice to Proceed	0	MI	25SEP03		-24
MI1020	Begin Construction	0	MI	17MAY04		-5
MI1040	Winter Constraint 2004	0	MI	17MAY04*		-5
MI9995	Substantial Project Completion	0	MI		17NOV04	-17
MI9999	Final Project Completion	0	MI		02DEC04	-24
Design and Permits						
DE2000	Survey Road & Site	15	OW	25SEP03	15OCT03	-22
DE2005	Delevoped Site Plan (For Permits)	10	OW	16OCT03	29OCT03	-22
DE2010	Design	30	OW	16OCT03	26NOV03	120
DE2020	Permits - Submit	5	OW	30OCT03	05NOV03	-22
DE2030	Permits - Approved	80	OW	06NOV03	01MAR04	-22
Project Management						
PM3000	Release Wind Turbines for Fabrication	5	PM	02MAR04	08MAR04	-22
PM3010	Receive Wind Turbines	130	PM	09MAR04	08SEP04	-24
Construction						
Project General						
PG1000	Mobilize	5	PM	17MAY04	21MAY04	-5

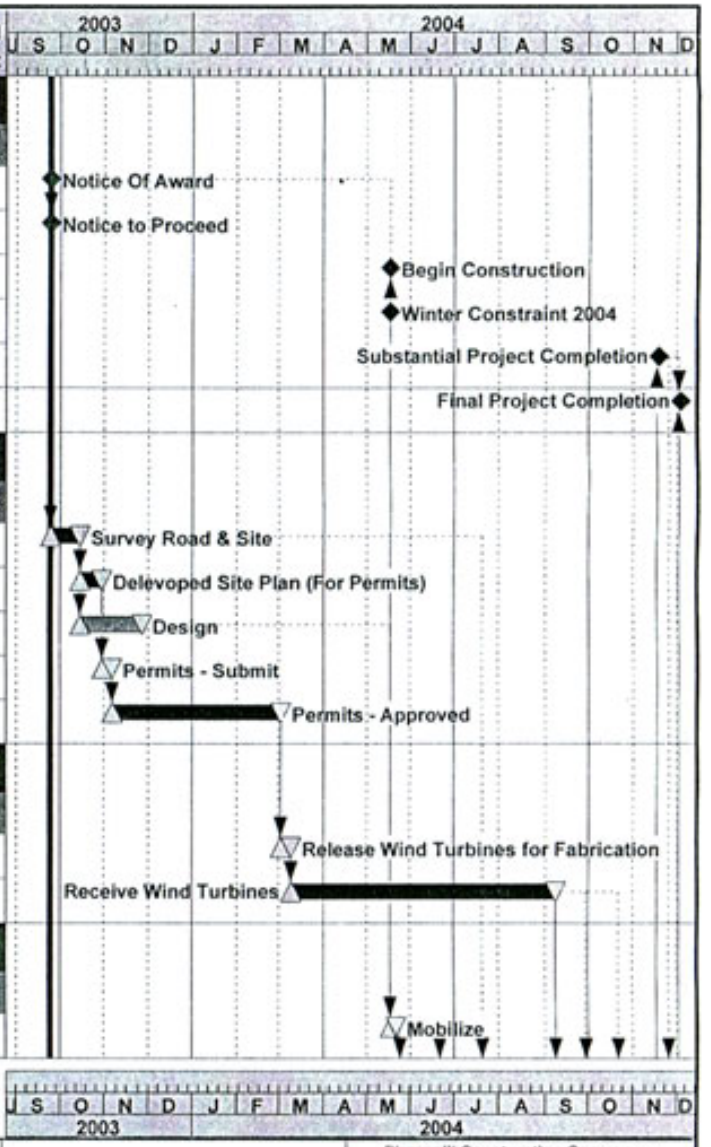

Start Date	25SEP03
Finish Date	02DEC04
Data Date	25SEP03
Run Date	02OCT03 16:49

Early Bar
Progress Bar
Critical Activity

WT1A Sheet 1 of 3

East Mtn Wind Turbines - Prelim #1
East Haven Wind Farm
Preliminary Project Schedule

pizzagalli construction company

Pizzagalli Construction Company -

Date	Revision	Checker	Approve

© Primavera Systems, Inc.

FILE COPY

EHWF-MR-14

Activity ID	Activity Description	Orig Dur	Resp	Early Start	Early Finish	Total Float
Project General						
PG9999	Project Close-Out & Demobilization	5	PM	26NOV04	02DEC04	-24
Site Work						
SI1000	Clear Trees Along Access Road	20	SI	25MAY04	21JUN04	4
SI1040	Demo Existing Structures	20	CD	25MAY04	21JUN04	-5
SI1020	Overhead Power Line Work	40	EL	25MAY04	19JUL04	76
SI1050	Foundation Excavation (#4)	10	SI	22JUN04	05JUL04	-5
SI1140	Foundation Excavation (#1)	15	SI	22JUN04	12JUL04	25
SI1030	Underground Elect Ductbank	20	EL	22JUN04	19JUL04	76
SI1010	Rework/Reconst Access Road	30	SI	22JUN04	02AUG04	4
SI1070	Concrete Foundation Work (#4)	10	CO	06JUL04	19JUL04	0
SI1080	Foundation Excavation (#3)	10	SI	06JUL04	19JUL04	-5
SI1160	Concrete Foundation Work (#1)	10	CO	13JUL04	26JUL04	25
SI1075	Cure Concrete Foundation (#4)	7	CO	20JUL04	28JUL04	0
SI1110	Foundation Excavation (#2)	10	SI	20JUL04	02AUG04	-5
SI1165	Cure Concrete Foundation (#1)	7	CO	27JUL04	04AUG04	27
SI1060	Install Rock Anchors (# 4)	7	SI	29JUL04	06AUG04	0
SI1100	Concrete Foundation Work (#3)	10	CO	03AUG04	16AUG04	-5
SI1150	Install Rock Anchors (#1)	7	SI	05AUG04	13AUG04	27
SI1105	Cure Concrete Foundation (#3)	7	CO	17AUG04	25AUG04	-5
SI1130	Concrete Foundation Work (#2)	10	CO	17AUG04	30AUG04	0
SI1090	Install Rock Anchors (#3)	7	SI	26AUG04	03SEP04	-5
SI1135	Cure Concrete Foundation (#2)	7	CO	31AUG04	09SEP04	0
SI1170	Install Turbine #4	15	ME	09SEP04	29SEP04	-24
SI1200	Install Turbine #1	15	ME	09SEP04	29SEP04	8
SI1120	Install Rock Anchors (#2)	7	SI	10SEP04	20SEP04	0
SI1210	Commission/Start-up Turbine #4	5	SU	30SEP04	06OCT04	3
SI1213	Commission/Start-up Turbine #1	5	SU	30SEP04	06OCT04	13

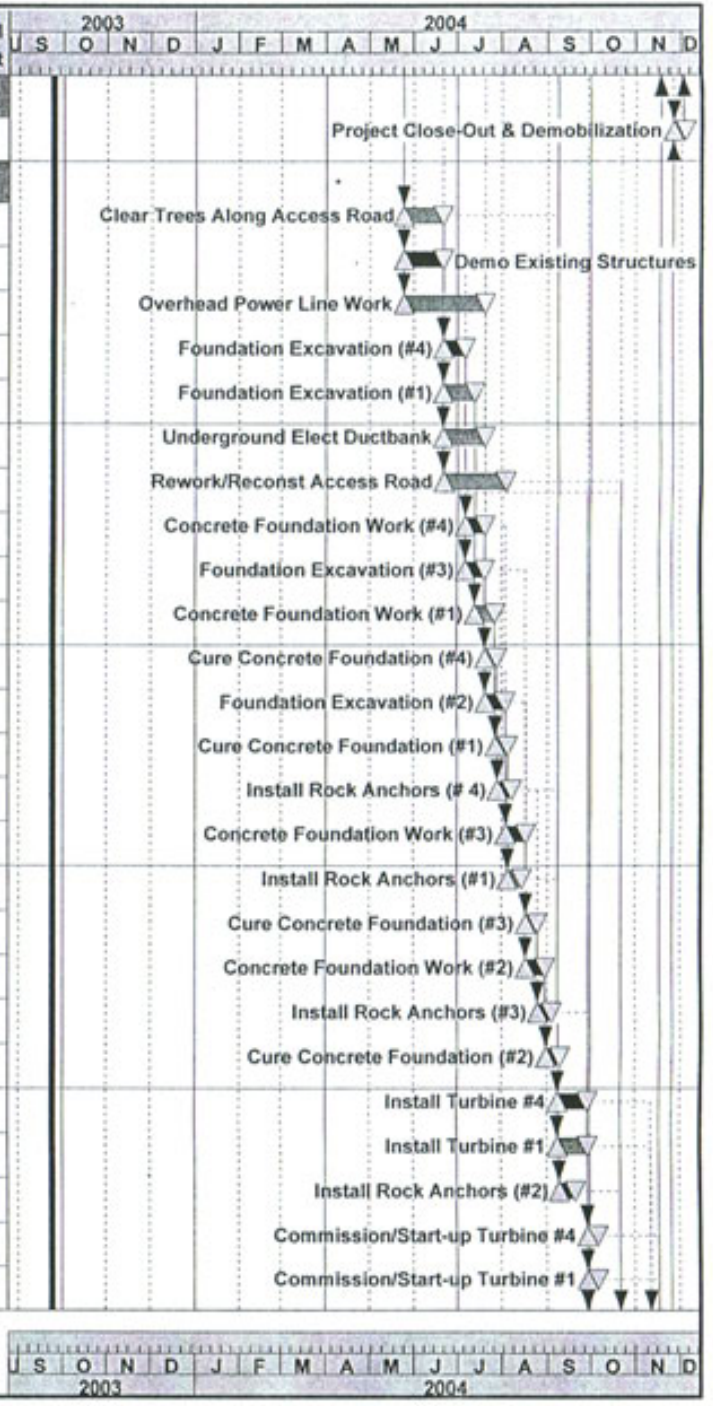
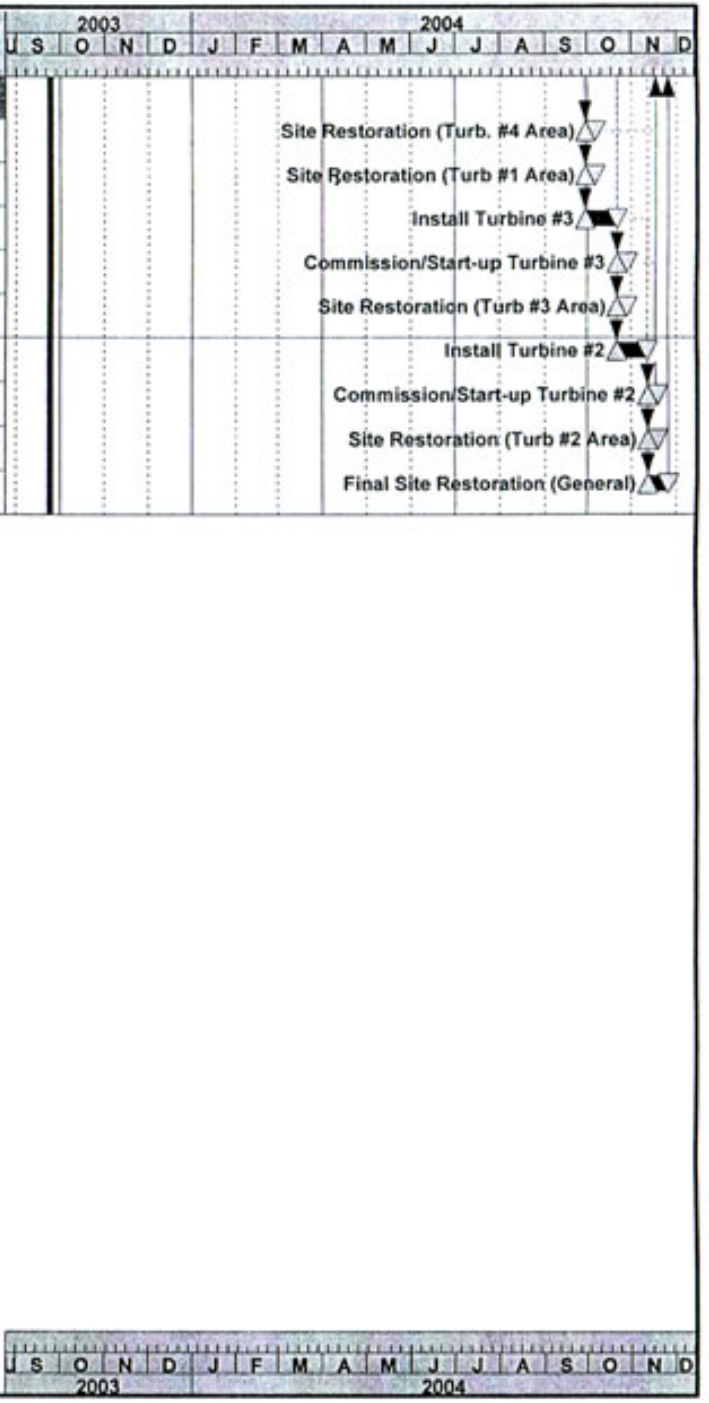
Activity ID	Activity Description	Orig Dur	Resp	Early Start	Early Finish	Total Float
Site Work						
SI1220	Site Restoration (Turb. #4 Area)	5	SI	30SEP04	06OCT04	13
SI1250	Site Restoration (Turb #1 Area)	5	SI	30SEP04	06OCT04	18
SI1180	Install Turbine #3	15	ME	30SEP04	20OCT04	-22
SI1211	Commission/Start-up Turbine #3	5	SU	21OCT04	27OCT04	-7
SI1230	Site Restoration (Turb #3 Area)	5	SI	21OCT04	27OCT04	3
SI1190	Install Turbine #2	15	ME	21OCT04	10NOV04	-22
SI1212	Commission/Start-up Turbine #2	5	SU	11NOV04	17NOV04	-17
SI1240	Site Restoration (Turb #2 Area)	5	SI	11NOV04	17NOV04	-12
SI1260	Final Site Restoration (General)	10	SI	11NOV04	24NOV04	-22
